

#### PLANNING AND CONSTRUCTION DEPARTMENT

1130 Fifth Avenue, Chula Vista, CA 91911 (619) 691-5553 FAX (619) 420-0333



# PROPOSITION O PROJECT UPDATES

### Feb, 2015 CBOC Meeting

This report provides a status report of projects that are part of the Proposition O Program part of the Capital Facility Financing Plan (CFFP). It is intended to provide information to the Citizens' Bond Oversight Committee (CBOC), Board of Trustees, staff and public regarding Proposition O expenditures. Project status is the status around the first of the month that this report is dated.

Financial information is provided in a separate report and in the monthly CFFP board agenda item.

The list of projects is divided into Active Projects and Completed Projects (including projects in the close-out process). The active projects are listed in the same order as the CFFP report. Updated project information is highlighted.

#### **ACTIVE PROJECTS**

## Chula Vista High School:

CVH ORG Title IX Team Room	A/E: <i>RNT</i>	Design: 70%
Contractor: tbd	Construction: 0%	Change Order Rate: 0%

This portion of the CVH ORG Projects consists of a softball team room similar to the MVH Title IX project. Design is under way and the intent is to have the project complete before the spring 2015 softball season, however actual completion depends on DSA approval timelines.

## Mar Vista High School:

MVH Project 2 – Building 600	A/E: Platt Whit	telaw	Design: DSA Approved
Contractor: Whillock Contracting, Inc.	Construction: 20	<mark>0%</mark>	Change Order Rate: 0%

The work is modernization of special education classrooms in Bldg. 600. Construction began in late November.

Underground work continues. Rough plumbing is complete. Interior framing and rough electrical are in

progress. Occupancy is expected in fall 2015.



Building 600

# MVH Project 2 – Deferred Maintenance Electrical Upgrade A/E: Platt Whitelaw Contractor: Precision Electric Construction: 40% Change Order Rate: 0%

Campus-wide upgrade of the electrical grounding system. Underground and building conduit work was completed during the winter break. The contractor will come back during spring break to complete the wiring part of the project. Final completion is expected in summer 2015.

# Montgomery High School:

MOH Gym Structural Upgrades	A/E: Burkett & Wong	Design: 95% in DSA
Contractor: tbd	Construction: 0%	Change Order Rate: 0%

The project consists of structural upgrades recommended in the seismic review of this building and includes: repair cracking in the concrete walls and improve the anchoring of roof top equipment. Design documents have been submitted to DSA for their review and approval. DSA back-check is scheduled for February 11<sup>th</sup> and construction is planned for summer break.

MOH Title IX	A/E: Lord Architects, Inc.	Design: 50%
Contractor: tbd	Construction: 0 %	Change Order Rate: 0%

The original Title IX scope was for softball dugouts and replacement of the non-conforming baseball dugouts. Addition work required by Title IX includes new backstops, softball outfield fencing, storage for the softball and baseball fields, new field level concession stand and rest rooms for softball, upgrading accessible routes to both fields and bleacher modifications for accessibility.. The lack of utilities near the softball field increases the cost significantly. Continuation of design is dependent on a budget adjustment for the increased scope of work.

## National City Middle School:

NCM Project 2	A	A/E: <i>LPA</i>	Design: <b>DSA approved</b>
P2 Contractor: McCa	<i>rthy</i>	Construction: 100%	Change Order Rate: 8.1%
Parking lot Contracto	<mark>r: <i>Whillock</i> C</mark>	Construction: 15%	Change Order Rate: 0%
-	A	A/E: <i>tbd</i>	Design: 0%
Field Contractor:	C	Construction: 0%	Change Order Rate: 0%

The burned temporary toilet building will be removed and stored at L St. until the district and Williams Scotsman can resolve who is liable for the fire. Parking Lot grading is complete, electrical work is in progress and completion is scheduled for mid-August. Selecting a designer for the field restoration is in progress. Board member Pike and CBOC Chair Marinovich and CBOC member Yamane toured the project on 1/30/15.



# Palomar High School:

PAH Project 1 - Science	A/E: <i>tbd</i>	Design: 0%
Contractor: tbd	Construction: 0%	Change Order Rate: 0%

A scoping meeting was held with the principal and science teachers on February 4th. Staff will evaluate the feasibility of the requested facilities and equipment.

#### Solar:

**PPA 2**: All solar installations are complete. The accessible parking issue at ELH will be addressed by SunPower during the spring break. The replacement of the GFI breaker at BVM is in progress.

## Southwest High School:

SOH Title	e IX	A/E: Burkett & Wong	Design: DSA Approved
	Contractor: various	Construction: 100%	Change Order Rate: 0%

The following work is complete:

- restoration of the infield
- new outfield fence
- ADA path of travel
- installation of power to the field and home dugout
- new scoreboard (certified by DSA on 1/28/15)

The batting cage is complete pitching machine was purchased.

Planning a multi-sport team room is in progress.



#### Southwest Middle School:

SOM Project 1B Increment 2	A/E: <i>RNT</i>	Design: DSA approved
Contractor: Whillock Const.	Construction: 95%	Change Order Rate: 5.0%

The contractor started construction on April 7<sup>th</sup>. This project includes renovation of the old shop buildings into two science classrooms, a new after school room and support areas. Completion is expected in late February but staff will not move in until the spring break.





SOM Project 1C – MPR & Bldg D	A/E: <i>RNT</i>	Design: <b>DSA approved</b>
Contractor: tbd	Construction: 0%	Change Order Rate: 0%

The project includes a full renovation of Building D (a single large classroom) and cosmetic improvements to the auditorium (MPR). Bidding is scheduled for March with construction scheduled to begin in April. The project is expected to be occupied in early 2016.

## Sweetwater Union High School:

SUH Stadium Track & Field	A/E: <i>RNT</i>	Design: DSA Approved
Field Contractor: Byrom-Davey	Construction: 100%	Change Order Rate: 0%
	A/E: <i>BakerNowicki</i>	Design: 0%
Concession Contractor: tbd	Construction: 0%	Change Order Rate: 0%
	A/E: tbd	Design: 0%
Title IX Upgrades Contractor: tbd	Construction: 0%	Change Order Rate: 0%
Title IX Practice Field Contractor:	Construction: 0%	Change Order Rate: 0%


Concession: The track and field project removed a non-conforming building. BakerNowicki Design Studio architects is the recommended design firm. Design and DSA approval are expected to take 6 months and bidding and construction about 6 months. Completion expected in spring 2016 depending on DSA approval timelines.

Title IX Upgrades: The project includes an ADA accessible path of travel, scoreboard, power, new pitching cage and batting cage.

Title IX practice field (upgrade of the field and relocation of a foul pole): This portion of the project is out to bid with completion expected in May.

<b>SUH Site</b>	<b>Restoration (Parking Lo</b>	ot Improvements)	A/E: Hector Reyes	Design: <b>DSA Approved</b>
	Parking Lot Contractor: tbd		Construction: 0 %	Change Order Rate: 0%
	Demolition Contractor: tbd		Construction: 0 %	Change Order Rate: 0%

This project includes demolition of the welding building and provides expanded parking for the site (214 spaces in the north lot). The project was approved by DSA on 10/15/14. DSA has voided the project because the architect let his license lapse. The architect renewed his license but the district has not been able to contact him. The project is on hold until the architect resubmits to DSA (he must pay the resubmittal fees) or the district elects to replace the architect. Construction completion is unknown at this time. The district will proceed with the demolition (including asbestos abatement) portion of the project; demolition is planned for summer break.

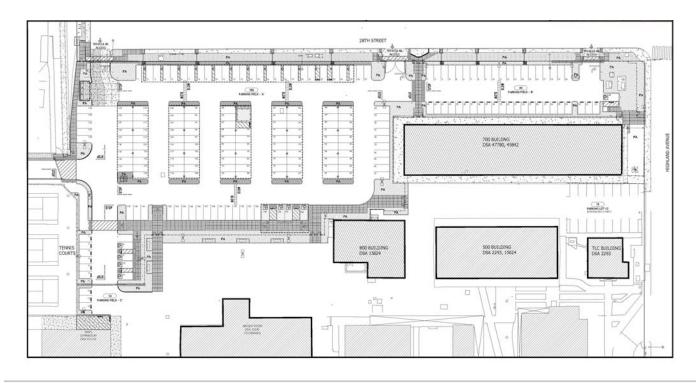





## Technology Infrastructure:

Technology Infrastructure	A/E: IT Department	Design: 100%
Contractor: Computer Protection	Construction: 100%	Change Order Rate: 0%
Technology, Inc.		
Contractor: Nexus IS, Inc.	Construction: 87%	Change Order Rate: 1.4%
Contractor: Standard Electronics	Construction: 87%	Change Order Rate: 4.4%

Uninterrupted power supply (UPS) replacement by Computer Protection Technology is complete.. Wireless access cabling and installation of data communication equipment has been substantially completed at 11 high schools. The remaining high schools (PAH, SOH and SUH) should be complete in March. The remaining middle schools (BVM, CVM, MOM, CVM, and RDM) should be complete by the end of June.

#### Various Sites:

# **Ceiling Fans**

Contractor: Farnum Electric	Construction: 0%	Change Order Rate: 0%
-----------------------------	------------------	-----------------------

Farnum Electric was the only bidder to install ceiling fans throughout the district in un-air-conditioned spaces.

#### PROJECTS ON HOLD – WAITING FOR CONSTRUCTION FUNDING

# Bonita Vista High School:

BVH Track & Field Design	A/E: NTD Architects	Design: DSA Approved
Contractor: tbd	Construction: 0 %	Change Order Rate: 0%

This project the design of an artificial track and field, electrical infrastructure for stadium lights, bleachers and restrooms was approved by DSA on June 5, 2014 and is on hold pending identification of funding for construction.



# Hilltop High School:

<b>HTH Trac</b>	k & Field Design	A/E: NTD Architects	Design: DSA Approved
(	Contractor: tbd	Construction: 0 %	Change Order Rate: 0%

This project for the design of an artificial track and field was approved by DSA on July 31, 2014 and is on hold pending identification of funding for construction.



#### **BUILDING GREEN with PROP O**

Chula Vista High Modernization Project 1 has received LEED Platinum certification from the US Green Building Council (Dec 2013).

Chula Vista Middle School Project 1 – pending

Hilltop High Modernization Project 1 has received LEED <u>Platinum</u> certification from the US Green Building Council (Dec 2013).

Mar Vista High Modernization Project 1 has received LEED Gold certification from the US Green Building Council (Jan 2014).

Montgomery High Modernization Project 1 has received LEED <u>Platinum</u> certification from the US Green Building Council (Dec 2013).

Montgomery Middle School Project 1 – pending energy credit for PV. On track for LEED Platinum.

National City Middle School Project 1 has received LEED Gold certification from the US Green Building Council (Feb 2014).

**Southwest High School Project 1** – pending.

**Southwest Middle School Project 1** – cannot be LEED certified.

Sweetwater Union High Modernization Project 1 has received LEED <u>Platinum</u> certification from the US Green Building Council (Dec 2013).

#### **COMPLETED PROJECTS**

#### **Prop O Close-out Phase Projects** (Architect, Contractor):

**BVM Modernization** (*IBI Group, Fordyce Construction, Change Order rate* 8.66%) – Complete. DSA closeout process in progress.

HTM Ceiling Fans (Farnum Electric and Price Electric; no change orders) – Complete (non-DSA project).

**CVH Interim Housing** (*BCA*, *Turner Construction*) – Closed without certification on 7/21/2011. Final documents will be submitted to DSA.

**CVH ORG Classroom Interior Upgrades** (RNT Architects, MA Stevens, CO rate 8.6%) – Work is complete.

Fire Alarm Upgrades – Group 2 – NCM (LPA, McCarthy) – Certified on 1/16/15.

**Fire Alarm Upgrades Group 3 – BVH, BVM, CPH, CPM, ELH, GJH, HTM, MVM, MOM, and PAH** (*Johnson Consulting Engineers, Time and Alarm Systems, CO rate* 9.0%) – Complete and in the close-out phase with DSA. ELH Certified 11/25/14. CPM Certified on 12/5/14. BVH and CPH certified on 12/8/14. BVM certified on 1/13/15. PAH certified on 1/14/15. NCM certified on 1/16/15. GJH, HTM, MVM, and MOM certified on 1/23/15.

Fire Alarm Upgrades – Group 4 – MVH & SOH (LPA, Standard Electronics, CO rate 1.1%) – Complete and in DSA closeout process.

GJH Health Clinic Upgrades (Matalon, Kinsman Construction) – Certified on 1/22/15.

#### **Power Purchase Agreement (PPA) Solar Power Projects:**

**PPA2 Solar at BVM** (SunPower) – Complete and in the close-out phase with DSA.

**PPA2 Solar at ELH** (SunPower) – Complete and in the close-out phase with DSA.

**PPA2 Solar at GJH** (SunPower) – Complete and in the close-out phase with DSA.

**PPA2 Solar at HTM** (SunPower) – Complete and in the close-out phase with DSA.

**PPA2 Solar at RDM** (SunPower) – Complete and in the close-out phase with DSA.

**PPA2 Solar at SOM** (SunPower) – Complete and in the close-out phase with DSA.

**SOM Project 1and 1A** (*LPA*, *HAR*, *terminated on 6/21/11*, *GEM Industrial*) – HAR Construction terminated on June 21, 2011; in litigation. Complete and in the close-out phase with DSA.

**SOM Project 1B Increment 1** (*RNT*, *APR terminated*) – Complete and in the close-out phase with DSA.

**SUH Artificial Track and Field** (*RNT*, *Byrom-Davey*) – Complete and in the close-out phase with DSA. The Ribbon Cutting Ceremony was on October 11, 2013.

**SUH Welding Building 2b** (*Hector Reyes, Farnum Elec., CO Rate is 0%*) – Complete and in the close-out phase with DSA.

#### Prop BB Close-out Phase Projects:

**CPH 6 Portables (400)** (100048) – Certified on 4/14/14

**CPM Modernization** (107670) - Closed without certification on 7/21/2011. Documents have been submitted to DSA and we are awaiting certification.

**GJH 8 Portables** (106555) – Closed without certification on 3/21/2008. Architect is gathering documents for closeout.

**SOH 1 Portable** (106627) – Closed without certification on 1/15/2008. Need to submit documents to DSA.

**SOH Portables** (111931) – Portables have been removed which means that the project can be voided after certification of the SOH restroom.

**SOH Restroom Portable** (111931) – Documents will be submitted for DSA certification.

# <u>Prop O (& BB) Completed Projects Certified by the Division of State Architect (DSA):</u>

DIZII	D DDM 1	C .: C 1 7/20/00
BVH	Prop BB Mod	Certified on 7/28/08
BVH	Prop BB Mod 200N 200S	Certified on 10/7/08
BVH	Prop BB Lunch Shelter	Certified on 10/28/09
BVH	Bleacher Replacement	Certified on 10/28/09
BVH	HVAC upgrades	Certified on 5/12/14
BVH	Fire Alarm Upgrade	Certified on 12/8/14
<b>BVM</b>	Fire Alarm Upgrade	Certified on 1/13/15
CPH	Prop BB Project 1A	Certified on 9/12/13
CPH	Prop BB Project 1B	Certified on 6/12/13
CPH	Prop BB Project 1C	Certified on 10/27/09
CPH	Prop BB Lunch Shelter	Certified on 6/30/09
<b>CPH</b>	Prop BB 6 portables and Bldg 400	Certified on 4/14/14
CPH	Prop O Title IX Portables	Certified on 4/17/14
CPH	Prop O Title IX Gym Door	Certified on 8/5/14
CPH	Fire Alarm Upgrade	Certified on 12/8/14
CPM	Fire Alarm Upgrade	Certified on 12/5/14
CVH	Prop BB Project 1A	Certified on 2/24/11
CVH	Prop BB Project 1B	Certified on 7/21/11
CVH	Prop BB 2-story CR Bldg	Certified on 2/24/11
CVH	Stadium Repairs	Certified on 5/29/09
CVH	Prop O Project 1	Certified on 4/25/12
CVH	Fire Alarm Upgrades	Certified on 10/10/14
CVM	Prop O Project 1	Certified on 8/27/13
CVM	Portable Upgrade	Certified on 8/28/13
CVM	Fire Alarm Upgrade	Certified on 6/27/14
ELH	Fire Alarm Upgrade	Certified on 11/25/14
GJH	Prop BB Mod 3 buildings	Certified on 7/21/11
GJH	Health Center	Certified on 2/24/11
<b>GJH</b>	Health Center Upgrades	Certified on 1/22/15
<mark>GJH</mark>	Fire Alarm Upgrade	Certified on 1/23/15
HTH	Prop BB 2-story CR Bldg	Certified on 9/26/11
HTH	Prop BB Project 1A	Certified on 10/13/11
HTH	Bleacher Replacement	Certified on 10/28/08
HTH	Scoreboard Replacement	Certified on 2/6/14
HTH	Interim Housing	Closed on 3/10/14
	6	

HTH	Prop O Project 1	Certified on 6/25/13
HTH	Interim Housing Removal	Certified on 8/7/13
HTH	Title IX Field and Restroom	Certified on 4/1/14
HTH	Fire Alarm Upgrade	Certified on 8/28/14
HTM	Shade Structure and Modernization	Certified on 9/14/12
HTM	Fire Alarm Upgrade	Certified on 1/23/15
MOH	Prop BB Interim Housing	Closed on 3/7/11
MOH	Prop O Project 1	Certified on 6/11/13
MOH	Prop O Scoreboard	Certified on 10/14/13
MOH	Interim Housing	Certified on 10/27/09
MOH	Interim Housing Removal & Basketball Courts	Certified on 4/29/13
MOH	Prop O Project 1 Shade Structures	Certified on 3/25/14
MOH	Fire Alarm Upgrade	Certified on 8/28/14
MOH	Prop O Project 2	Certified on 12/10/14
MOH	Prop O Project 2 Mod & 800 Demo	Certified on 11/21/14
MOM	Prop BB Building J	Certified on 7/10/08
MOM	Interim Housing	Certified on 8/10/10
MOM	Interim Housing Restroom	Certified on 7/15/11
MOM	Interim Housing Library	Certified on 8/17/12
MOM	Prop O Project 1	Certified on 12/10/14
<b>MOM</b>	Fire Alarm Upgrade	Certified on 1/23/15
MVH	Interim Housing	Certified on 2/24/11
MVH	Prop O Project 1	Certified on 4/30/14
MVH	Title IX Upgrades	Certified on 4/17/14
<mark>MVM</mark>	Fire Alarm Upgrade	Certified on 1/23/15
NCM	Interim Housing	Certified on 2/22/10
NCM	Prop O Project 1	Certified on 5/15/14
<b>NCM</b>	Fire Alarm Upgrade	Certified on 1/16/15
PAH	Prop BB Portables	Certified on 7/14/08
<mark>PAH</mark>	Fire Alarm Upgrade	Certified on 1/14/15
PPA 1	Solar at BVH, CPH	Certified on 2/19/14
PPA 1	Solar at MOH, SOH	Certified on 1/15/14
PPA 1	Solar at CVH, ORH	Certified on 4/21/14.
PPA 2	Solar at CPM	Certified on 7/10/14
PPA 2	Solar at CVM	Certified on 10/9/14
PPA 2	Solar at ELM	Certified on 7/17/14
PPA 2	Solar at HTH	Certified on 10/9/14

PPA 2	Solar at HTH Roofs	Certified on 10/9/14
PPA 2	Solar at MVH	Certified on 8/18/14
PPA 2	Solar at OLH	Certified on 6/30/14
PPA 2	Solar at ORH	Certified on 10/15/14
PPA 2	Solar at SUH	Certified on 8/18/14
PPA 2	Solar at SYH	Certified on 8/18/14
SOH	Prop BB 400 Building	Certified on 7/28/11
SOH	Prop BB 6 portables	Closed on 10/22/13
SOH	Prop O Project 1	Certified on 8/23/13
<b>SOH</b>	Title IX Scoreboard	Certified on 1/28/15
SOM	Interim Housing	Certified on 7/28/11
SOM	Fire Alarm Upgrade	Certified on 5/15/14
SUH	3 portables (since removed)	Closed by DSA on 9/20/13
SUH	Stadium Repairs	Certified on 5/29/09
SUH	Interim Housing	Certified on 7/21/11
SUH	Prop O Project 1	Certified on 12/3/13

# Prop O Completed Projects (non-DSA projects):

CVH	ORG Portable Removal	Portables were removed during construction of Project 1 and the last portables removed in April 2013.
CVH	ORG Backstop & Fencing	Complete 5/30/14
<b>CVH</b>	ORG Building 100, 500 Upgrades	Complete 9/1/14
PPA2	Solar at MVH Ground mounted	Complete
SOM	Field Renovation	Complete
SOM	Site Improvements	Complete 12/12/11
SUH	ORG Portable Removal	Portables were removed in Jan 2012.
SUH	Bldg 100 HVAC Upgrades	Complete April 2014

# Acronyms (other than school sites):

ADA	Americans with Disability Act	LEED	Leadership in Energy & Environmental Design
DSA	Division of State Architect	LPA	LPA, Inc. Architects
BAN	Bond Anticipation Note	Mod	Modernization
BCA	Bunton Clifford Architects	MPR	Multi-purpose Room
BOT	Board of Trustees	NTD	NTD Architects
CBOC	Citizens' Bond Oversight Committee	ORG	Overcrowded Relief Grant (state funding program)
CFFP	Capital Facilities Financing Plan	PPA	Power Purchase Agreement
CHPS	Collaborative for High Performance Schools	PWA	Platt Whitelaw Architects
CR	Classroom	RNT	Roesling Nakamura Terada Architects
DSA	Division of State Architect	RRC	Ruhnau Ruhnau Clarke Architects
GFI	Ground Fault Interrupter	USGBC	US Green Building Council
HVAC	Heating, Ventilating and Air Conditioning	ZTA	Zagrodnik + Thomas Architects
IT	Information Technology	tbd	to be determined
